

AGILE GUIDELINES

Processes and Templates to apply Agile Scrum Delivery

written by: Eccles, Gherardini,
Magni, Slager
unit:
review:

approved by:
Manuela Nelli
doc ID:
issue date:

doc. model

MDE_GEN_TEC_001 1.2

Privacy notes: Confidential, only for Internal Use

REPLY

Via Castellanza, 11 - 20151 Milano - tel. +39.02.535761 - fax. +39.02.53576444
Via Cardinal Massaia, 71 - 10147 Torino - tel. +39.011.19699100 - fax. +39.011.19699101
Via Cardinal Massaia, 83 - 10147 Torino - tel. +39.011.29100 - fax. +39.011.2911009
V.le Regina Margherita, 8 - 00198 Roma - tel. +39.06.844341 - fax. +39.06.84434400
Via del Giorgione, 15 - 00147 Roma - tel. +39.06.844341 - fax. +39.06.84434599

www.reply.com

Processes and templates to apply Scrum

Review	Date	Changes	(Approved by)
1.0	06/2016	First Release	
2.0	08/2017	Review of the first version to synthesize the guidelines and splitting in two different documents (one for Agile and one for Scrumfall)	

Main changes list compared to the previous version:

Contents

PROCESSES AND TEMPLATES TO APPLY AGILE SCRUM DELIVERY	1
1 INTRODUCTION	4
1.1 PURPOSE	4
1.2 CONTENTS	4
1.3 HOW TO USE THIS GUIDE	5
2 PROCESS OVERVIEW	6
3 PROCESS DESCRIPTION	7
3.1 OFFERING	7
3.2 EXECUTION	10
3.3 CLOSURE	17
4 TOOLS & PRACTICES	19
4.1 USING JIRA EXAMPLE	19
4.1.1 INTRODUCTION	19
4.1.2 MAPPING PROCESSES AND DOCUMENT ON JIRA	19
4.1.3 BACKLOG HIERARCHY (EPICS -> USER STORIES -> TASKS)	20
4.1.4 SPRINT PLANNING	21
4.1.5 SPRINT REVIEW	21
4.2 GECO MANAGEMENT	22

1 INTRODUCTION

1.1 Purpose

The purpose of this document is to define a standard approach to Agile software delivery within the Reply Group. This document describes the guidelines for managing Agile projects in the context of the overall lifecycle of client engagement from Offer through to Closure.

Reply are endorsing the use of Scrum as the agile approach for iterative and incremental software development. The term “Agile” is a more a generic term to describe the iterative nature of delivery, whereas “Scrum” is an explicit approach to software development, both maybe used interchangeably throughout this document and should be considered the same. This document avoids describing or changing the Agile Scrum principles in detail but puts emphasis of the adoption of Agile Scrum within the context of a standard Project delivery that all Project Managers can leverage.

If you want to learn more about Scrum you can:

- read or download the "The Scrum Guide" available at <http://www.scrumguides.org/scrum-guide.html>
- refer to the Scrum Alliance <https://www.scrumalliance.org/> that is a primary source for Scrum definition and is depicted by the following diagram:



1.2 Contents

The document is largely broken into parts:

- (1) **Overall Process flow and Process description** of Agile aspects along including references to standardized templates to be used.
- (2) **Example References** to some of the main tools & practices that should be adopted for successful Agile execution.

AGILE GUIDELINES

Processes and templates to apply Scrum

1.3 How to use this guide

Next sections describe step-by step all activities needed in each project stage.

According to the Agile principles, the “Execution” phase can be tailored according to the specific context. This section generalizes the Lessons Learned of Reply from years in agile projects and provides a guidance.

The “Offering” and “Closure” phases must be executed according to recommendations of this document. The Agile projects can be very risky and the Agile conditions should be carefully evaluated; the guidelines are a support for evaluating and mitigating the risks mainly for the “fixed-price” projects.

Templates

For the Economic Offer you must use Reply templates that follow the legislation of each country, for the other stages you can choose to use Reply template or other templates (e.g. customer template when provided). Even if you decide to use a different template, you can use these guidelines and templates as operational checklist.

written by: Eccles,
Gherardini, Magni,
Slager
unit:

approved by: Manuela
Nelli

issue date:

review

page: 5/22

privacy note: Confidential, only for Internal Use

AGILE GUIDELINES

Processes and templates to apply Scrum

2 PROCESS OVERVIEW

In a typical client engagement model a Reply company would normally start engagement with a prospective client from RFP response Offer into Development, though to engagement Closure (though the lines between the phases are sometimes blurred with the introduction of “Discovery” and “Support” activities).

Scrum is considered for the main Development Phase, for the Development Team to organize their work and relate with the Customer during project execution.

In most engagements, we recognize 3 Types of Agile Orientated customers

- **Agile-Centric** – customer has a deep understand of Agile approach and practices
- **Agile-Potential** – customer either wants to or does not fully understand the values of agile
- **Non-Agile** – customer has no interest in the mechanisms of Agile delivery and are tuned to waterfall tracking practices.

Agile Centric customers will relate and adopt to Scrum quickly, however for Non-Agile customers aligned to waterfall based projects there is a need to wrap up the Agile Development practices into a more traditional waterfall approach centered around key milestone tracking, the term Scrumfall is given.

Those customers that are Agile-potential will require support to be transformed, this type of engagement would typically require an extra level of consultation from Reply to help them understand and transform through coaching.

The adoption of Agile practices have the greatest influence on the Development phase, though this document describes the end to end process in order to help Replyers Project Managers in the management of all project phases.

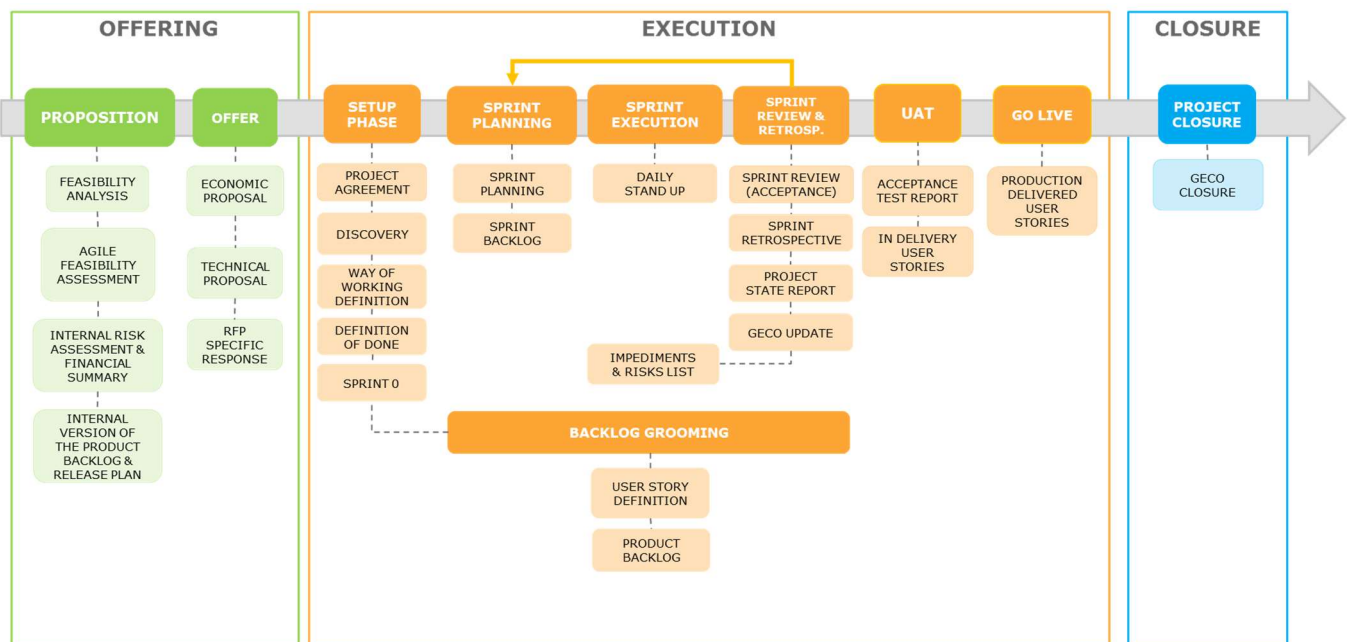


Figure 1 - Process Overview

written by: Eccles,
Gherardini, Magni,
Slager
unit:

approved by: Manuela
Nelli

issue date:

review

page: 6/22


privacy note: Confidential, only for Internal Use



3 PROCESS DESCRIPTION

In this section of the document a more elaborated explanation of each stage of the Process is described. For each stage, the document details actors involved, needed activities and the templates to be used.

3.1 Offering

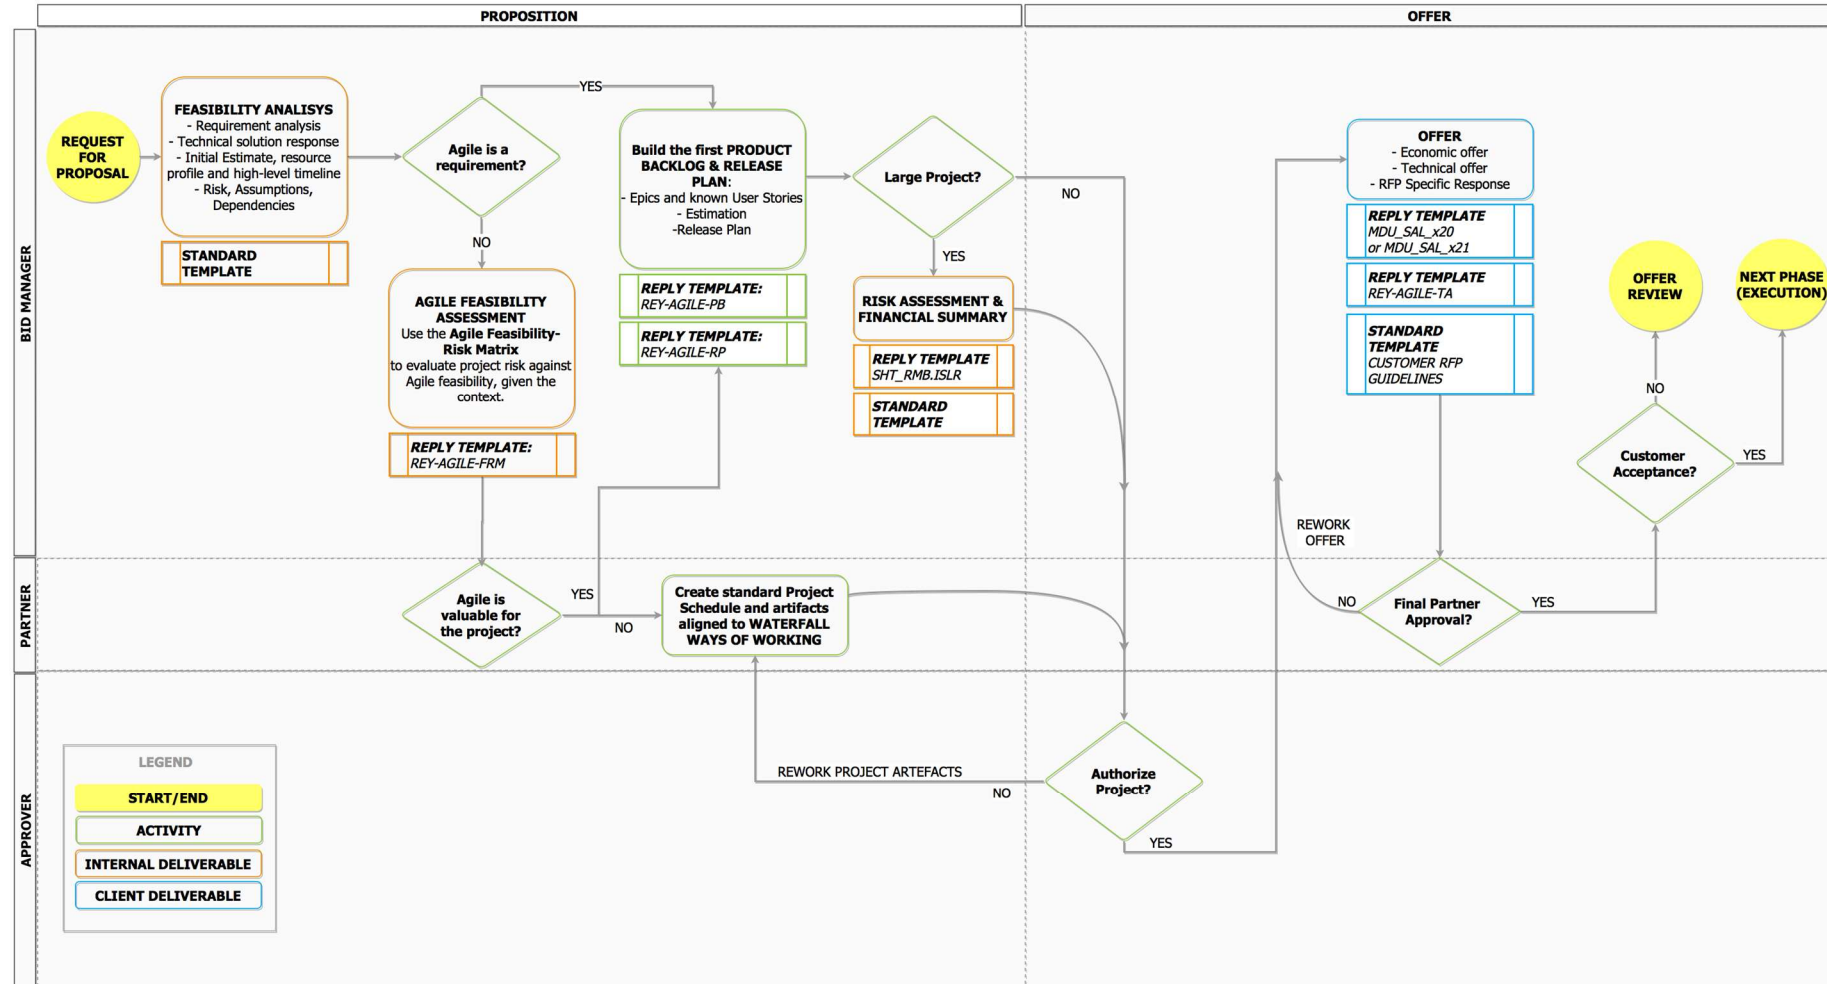



Actors:

- **Bid Manager:** is responsible for all the activities regarding RFP analysis and Offer composition. Usually supported by the bid team with different skills and competences
- **Partner:** reviews and sign the Offer. Is in charge to decide if it is the case to propose Agile development even if it is not required in the RFP
- **Approver:** formally authorizes to perform the project. Depending on the project size, either Partner, an Execute Partner or the CEO

Proposition

Request For Proposal: The process starts with the Customer issuing an RFP to Reply for a response.

Feasibility Analysis: This is the primary activity to pull together a comprehensive response in accordance to the stated RFP process lead by the Bid Manager, typically would include:

- Requirement Analysis
- Technical Solution Response
- Initial Estimate, Profiles and high-level timeline
- Risk, Assumptions, Dependencies

Agile Feasibility Assessment: Conduct Analysis on whether the project should be delivered using Agile Scrum methodology by the Bid Manager using the Agile feasibility/risk matrix, for the appropriate Partner to review and approve accordingly.

The Agile Feasibility-Risk Matrix aims at providing a common approach inside Reply for evaluating to what extent it might be worth moving to the Agile Methodology in addressing a project opportunity.

It based on assessing general drivers that have been identified as significant to assess a possible Agile context; a three-level scale is associated to each of them and, according to the dimension that is going to be analyzed (Feasibility or Risk), a value from 1 to 3 is mapped at each level.

- **Mapping Agile Suitability:** for each driver, it provides the level of "**Agile suitability**" related to each possible evaluation envisaged in the driver (from level value 1 meaning "less suitable" to value 3 meaning "more suitable")
- **Mapping Risk:** for each driver, it provides the level of "**Risk**" related to each possible evaluation envisaged in the driver (from level value 1 meaning "high risk" to value 3 meaning "low risk")
- **Feasibility-Risk Matrix:** according to the evaluation that the user will make for each driver, the tool will calculate a value to be mapped in the Risk Tolerance Matrix, that will give an indication regarding the convenience to move towards an Agile solution.
- **Risk Tolerance Matrix:** starting from the values obtained by the Feasibility-Risk Matrix, a graph will provide a number in the scale from 1 to 3 that represents the degree of confidence to move to an Agile solution proposal.

Internal Risk Assessment & Financial Summary: Separate to the RFP response an internally facing set of documents should be created, namely Risk Assessment and Financial Summary documents.

The Risk Assessment is very important and must be kept aligned in all project phases. The Financial Summary particularly targets projects over 300K (£300K or €300K) to ensure all the main commercial aspects have been thought of and covered before a formal RFP response has been submitted, there is no standardized document template but expected to include the following:

- Description of the project context
- For each project component: forecasted effort, costs, revenue & margin
- Cost & Revenue for each involved Reply company
- Third parties' services/products and supply conditions

written by: Eccles,
Gherardini, Magni,
Slager
unit:

approved by: Manuela
Nelli

review

issue date:

page: 8/22



- Payment terms, conditions and cash flow
- Warranties, insurance, penalties and deposits

Initial version of the Product Backlog & Release Plan: As part of the Requirements analysis the Bid Manager prepares an initial Product Backlog that aligns to key features to be developed, ideally with participation of the Customer (though in RFP response may not be appropriate).

Along with the initial estimations the Bid Manager (if expressly required or if he sees fit to the management of the initiative, mainly for fixed price projects) can create a Release Plan to build and overall timeline of delivery of the features, constrained by the planned headcount and timelines determined by the RFP. Unless already stated by the customer, the Bid Manager can establish a sequence of the feature delivery considered to be the most efficient for providing a competitive response.

Project Authorization: this activity is common to any project in Reply. Depending on the project size, the Approver can be a Partner, an Executive or the CEO.

Output Document	Distribution	Template Code
Feasibility Analysis	INTERNAL	No template provided. Use a standard template.
Agile Feasibility Risk matrix	INTERNAL	REPLY TEMPLATE: REY-AGILE-FRM
Product Backlog	INTERNAL (Input into RFP Response)	REPLY TEMPLATE: REY-AGILE-PB
Release Plan	INTERNAL (Input into RFP Response)	REPLY TEMPLATE: REY-AGILE-RP
Risk Assessment	INTERNAL	REPLY TEMPLATE: Sheet SHT_RMB.ISLR - Issues List (with risks) - This template is available in Classic Reply area of Reply Projects portal within ISRL – Issue List (with risks) section.
Financial Summary	INTERNAL	No Template. Word document with the above detailed mandatory information.

Offer Response

This phase manages the offer composition. For Agile projects the activities are the same as for a Waterfall project, but with different templates.

Offer: The Bid Manager prepares the Offer, which is divided into two documents:

- **Economic offer:** the scope of the economic offer is the same of the classic ones, plus an explicit characterization of who are the actors involved and their responsibilities.
- **Technical offer:** describes the solution from a technical point of view. The document is meant to share the design and software stack (servers, framework, libraries ...) will be used for the solution.
- **RFP Specific Response:** On occasion the customer may also have a predefined response template to adhere to (to compare responses), this could replace the above 2 documents or can be in addition to. Bid Manager should clarify with the customer on the Offer deliverables expected.

written by: Eccles,
Gherardini, Magni,
Slager
unit:

approved by: Manuela
Nelli

issue date:

review

page: 9/22



Partner Approval: The Offer is subject to the Partner Approval before sharing to the Customer.

Customer Acceptance: The Customer accepts formally the Offer. In case of reject, the Bid Manager is in charge to manage the situation and obtain feedback of the unsuccessful response.

Output Document	Distribution	Template Code
Economic Offer	EXTERNAL Shared with the customer	REPLY TEMPLATES*: Agile Fixed Price Variable Scope - MDU_SAL_x20 Agile Time and Material – MDU_SAL_x21
Technical Offer	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-TA
RFP Response	EXTERNAL Shared with the customer	Explicit RFP based response in accordance to customer RFP guidelines

Mandatory templates are marked with asterisk (*). In this case case you cannot use alternative templates, but you must use Reply templates.

3.2 Execution

The execution phase is where the adoption of traditional Scrum is used for Agile based projects, enriched with the activities regarding Time & Cost Management (using GeCo) and the deliverables to accomplish the formal relationship.

written by: Eccles,
Gherardini, Magni,
Slager
unit:

approved by: Manuela
Nelli


issue date:

review

page: 10/22

AGILE GUIDELINES

Processes and templates to apply Scrum

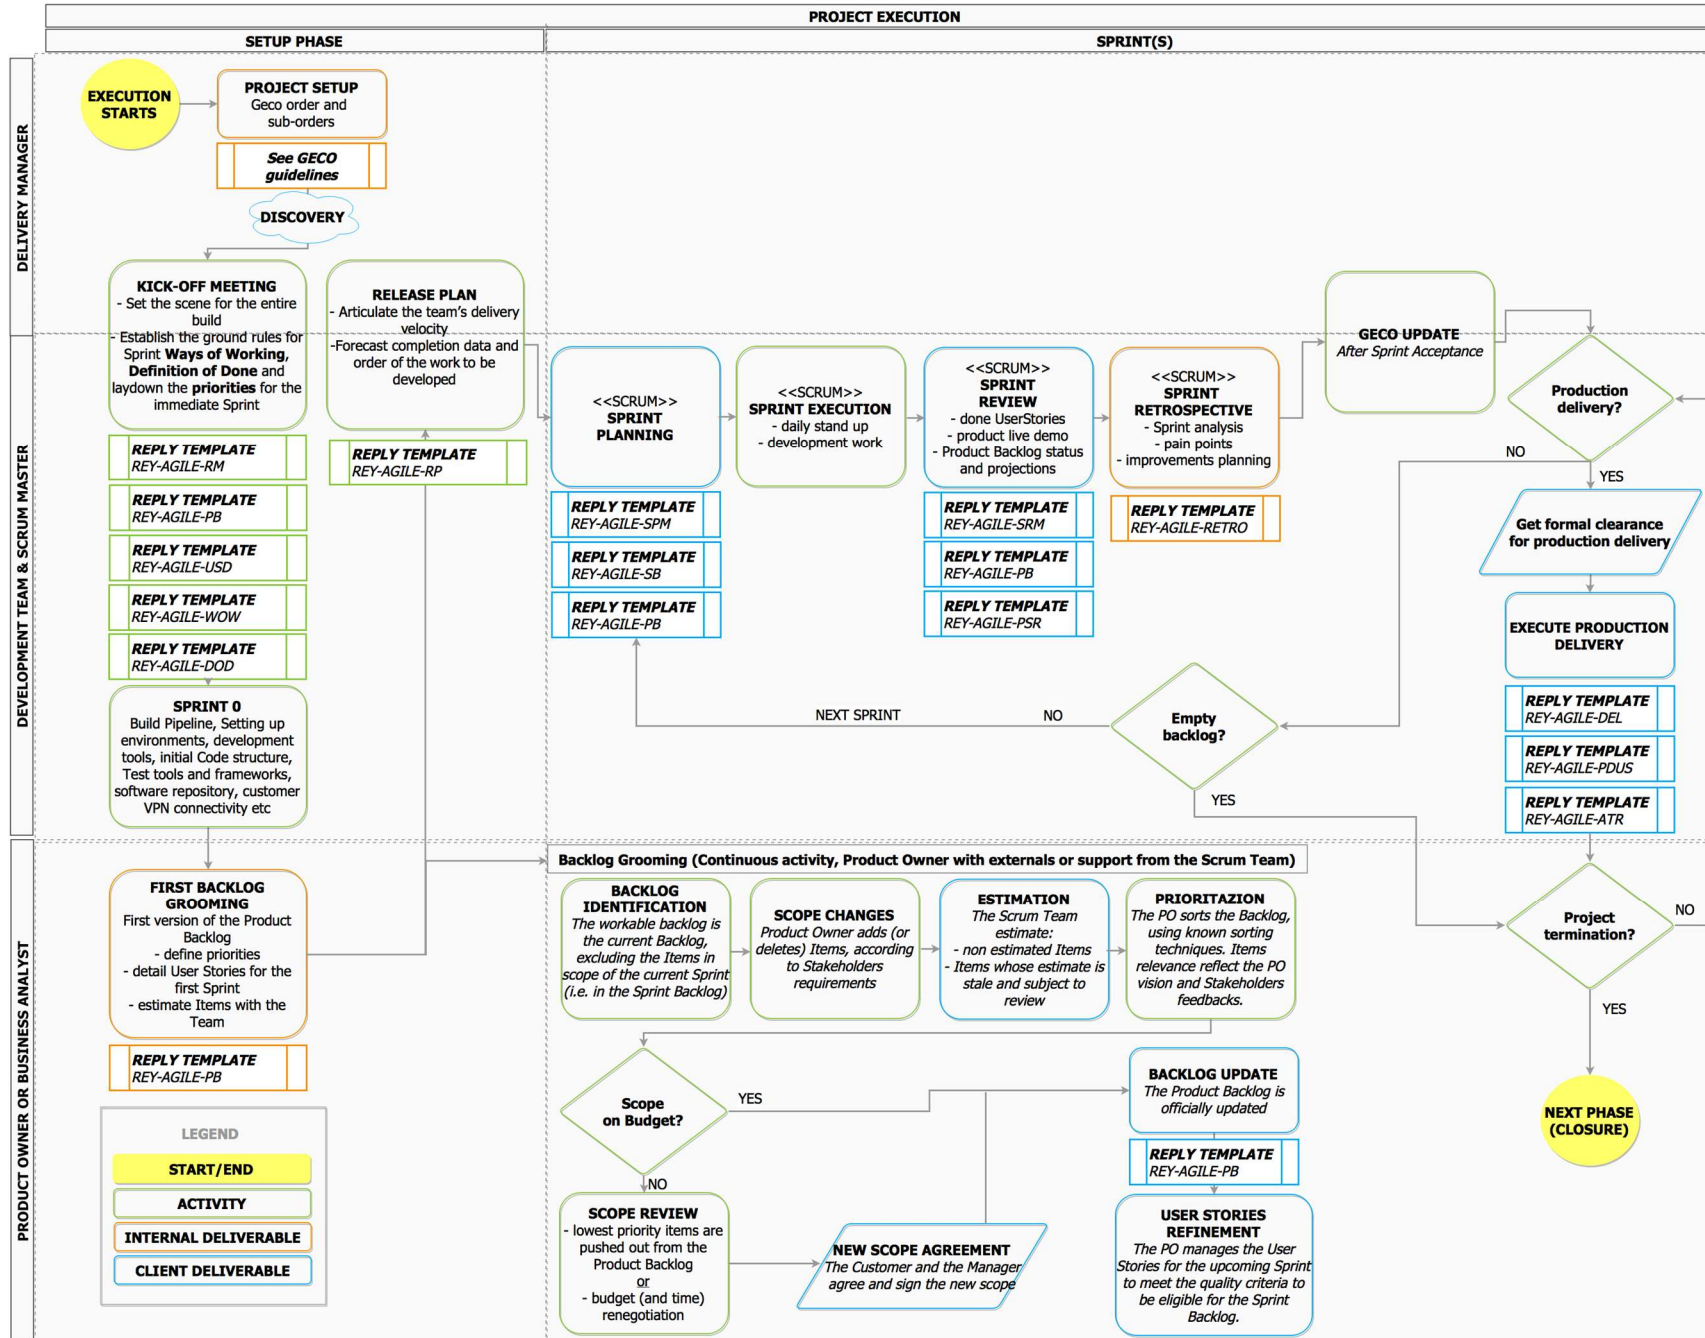



Actors:

- **Delivery Manager:** is not part of the Scrum team. The role is to mobilize the delivery team and set-up the accounting structure (Orders & Suborders) in GeCo. In case of small teams, he can delegate to the Scrum Master the GeCo suborder update activity. He is also involved in the budget and forecast review activities, at the end of each Sprint.
- **Scrum Master:** is an experienced Scrum practitioner from Reply. During project execution, the Scrum Master will be responsible driving the project forward in accordance to the agreed Ways of working and Definition of Done. In large projects with multiple Scrum Masters then an overall Delivery Manager will be identified to drive the project forward.
- **Development Team:** A team with all the appropriate technical and functional skills required for the project to design, develop and test the software necessary to fulfill the customer's requirements. In addition to standard software development, extra roles such as DevOps, Performance, Security, UI/UX may also be needed.
- **Product Owner or Business Analyst:** Ideally the role of the Product Owner will be played by the customer who will ultimately be accountable and is in a position to make decisions in order to deliver the highest valuable work in the required timeframe. In addition to this role a Business Analysis may either act as "Proxy" Product Owner interfacing with the customer business stakeholder or may complete the Product owner to translate the business needs for Technical Implementation.
- **Stakeholders:** communicate with the Product Owner the business needs, attend the Sprint Review meeting to get the status update and to give feedbacks on what has been done and the overall Product.

Setup phase

Project Setup: The Delivery Manager sets up GeCo order and suborders. Each Scrum Team involved in the project may have its own suborder. For each suborder, the Delivery Manager defines the overall budget and the forecast for the following three months and binds the Team to the suborder. Further details about GeCo setup and management are given in a dedicated section at the end of this document.

Discovery: For large projects or if requested by the customer a "Discovery Phase" is established to flesh out the requirements (through joint workshops with the customer), detail architectural design and detail out overall plan and price ahead of start of build and often a pre-require to establish a clear contract position. Discovery phases vary in size but are typically between 8 and 12 weeks in duration (and can be over 6 months duration).

Initial Kick-off Meeting: The initial kick-Off meeting run by the Scrum Master for the entire team and should set the scene for the entire build, establish the ground rules for Sprint Ways of Working, Definition of Done and laydown the priorities for the immediate Sprint.

Project Agreements document: This document is an output of the Kick-off meeting and defines the project goal, the team composition and the list of deliverables.

Ways of working (WoW) document: This document lays out the overall Scrum cycle, defining the during of sprints, ceremonies, process for acceptance, roles and responsibilities. It is a working document and can be amended through corrective action during the Sprint Retrospectives or at any time if the Scrum Team (including also the

written by: Eccles,
Gherardini, Magni,
Slager
unit:

approved by: Manuela
Nelli

issue date:

review

page: 12/22



Product Owner, usually provided by the customer) agrees on the change.

Definition of Done (DoD) document: This document defines the quality criteria in which the delivery is deemed acceptable to be considered as “DONE”. This will include criteria for outstanding defects, Static Analysis, Demos, Peer Reviews, Design Documents etc. It is a working document and can be amended through corrective action during the Sprint Retrospectives or at any time if the Scrum Team (including also the Product Owner, usually provided by the customer) agrees on the change.

Sprint 0: Often the first sprint “Sprint 0” is an important sprint and is geared towards bootstrapping the whole development process through the creation of the Build Pipeline, Setting up environments, Development Tools, initial Code structure, Test tools and frameworks, software repository, customer VPN connectivity etc. Basically, everything needed to be ready to implement. The duration of the first sprint depends on the project size. Typically, for a medium/large project this is a longer sprint cycle than normal maybe up to 4wks – 6wks in duration. For a small project instead, the first sprint is equal to other sprints. Even if is called “Sprint 0”, this optional stage differs from standard sprints and cannot be considered a real sprint because does not produce a reasonable product increment.

Product Backlog: The Product Owner or Business Analyst is accountable for the Product Backlog set-up, moreover is responsible ensuring the backlog is order in a way that meet Stakeholders’ needs and logical in terms of the software development sequence. The Product Backlog should always have User Stories/Backlog Items¹ ready to be implemented for each upcoming sprint, sometimes it is useful to have the backlog ready 2 sprints ahead to lock down any dependencies on the customer. To avoid waste, it is desirable that coarse-grained stories are broken down and prepared in a “just in time” fashion in case the effort is spent on work that is de-prioritized. Throughout the development phase the Product Backlog and its collection of user stories are groomed as part of Backlog Grooming.

Release Plan: The Scrum Master or Delivery Manager should maintain a Release Plan, shared with the Product Owner, throughout the development phase to articulate the team’s delivery velocity, forecast completion data and order of the work to be developed. The Release plan is an essential tool for large scale projects with high dependencies to synchronise work appropriately.

Output Document	Distribution	Template Code
Project agreements	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-RM
Product Backlog (definition)	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-PB
User Stories (definition)	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-USD
Ways of Working Definition	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-WOW

¹ With the “User Story” term, this document refers to the more generic Backlog Item.



Definition of Done	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-DOD
Release Plan	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-RP

Sprint(s)

The Team performs each Sprint as described within the Scrum framework, with no modification on the ceremonies (**Planning, Daily Stand-up, Demos & Retrospectives**).

Sprint Planning Meeting: This event is a planning event for the team along with the appropriate Product Owner to establish a plan for delivery for the next Sprint cycle.

It is important to note the **only** the Team can provide the commitment and can reject User Stories not ready for Development, the Planning ceremony covers typically:

- Confirm the immediate goals of the Sprint with Product Owner
- Review the backlog of work identified from the Product Backlog to ensure correct understanding
- Review the estimation/size of the work
- Determine based on the available capacity and velocity of what can be delivered
- Finalize the Sprint Backlog in terms of Commit & Stretch items
- Start the Sprint

Sprint Execution: this macro-activity addresses all the work performed by the Team executing the Sprint. The practices and events occurring inside a Sprint are defined through the Ways of Working Document and the Definition of Done. Typically, a workflow in an agile tool will be used to manage the User Stories from Ready for Development to Done. This stage includes also the integration/system tests in which the Development Team performs all the technical tests to validate the User Stories in scope for the delivery, according to the project agreements. Typically, the Team will assess:

- delivering User Stories to meet the acceptance criteria
- regression testing on User Stories already part of the Product
- overall software requirements to be met

Sprint Review: This is a review of the team's delivery contribution to show-case what they have achieved in the last Sprint it is also known as a "Demo" or "Show and Tell". Depending upon the Ways of working, the Sprint Reviews maybe a single event or multiple and can be used a part of Progressive Acceptance. Typically, though the Sprint Review happens on the last day of the Sprint and is used as an exit point for the next stage of the programme. In addition, Project Closure Reports or Project State Reports, are created as a quality statement and record of the deliver calling out all the features included, defects fixed, evidence of testing etc.

Sprint Retrospective: The retrospective ceremony happens after the sprint and ideally before the next Sprint planning session and is an internal team meeting, where the Team reflects on the last sprint and identifies things to continue to do along with improvements to further improve some aspects (e.g. velocity, quality and so on) for the next sprint. There are many different forms of presentation and tools that can be used but the main thing is that the team focus only a few items (2 or 3) to improve on for the next sprint, unless customer support is needed the internal

written by: Eccles,
Gherardini, Magni,
Slager
unit:

approved by: Manuela
Nelli

issue date:

review

page: 14/22



retrospective notes are not often shared externally.

GeCo update: The Delivery Manager (or sometimes in case of small teams the Scrum Master) updates GeCo suborder, according to what happened in the Sprint. At this stage the Delivery Manager accountable for the GeCo order should also review the overall project budget, according to Scrum Master feedbacks.

UAT (User Acceptance Test): The Product is tested to meet the functional and non-functional requirements, resulting in a certification for production delivery. The Product Owner is accountable for UAT execution and may be helped by a dedicated team of testers or by a set of real users. It is possible to perform UAT inside each sprint cycle as part of the sprint itself or separately from sprints through an ad-hoc session (typical in large projects). The overall testing and the not regression verification can be speeded up through the test automation.

Production Delivery: According to the different contexts, the production delivery can occur within the sprints cycle or can be separated from sprints (typical in large projects). In both cases is importance to highlight some significant activities of the delivery process.

Get formal clearance for production delivery: The Team triggers the production release process upon formal clearance from the Product Owner of Stakeholders, depending on the requirements within the Customer organization.

Execute production delivery: Going live with a Production Delivery maybe completed within working in hours or in case of being traffic impacting done out of hours. Typically, a Production Release document is created to detail the release process along with and risks and roll-back options in case of any challenges. Nowadays a greater emphasis on Continuous Delivery puts emphasis on a set of automated scripts maintained by DevOps personal to deploy changes in live.

Backlog Grooming/First Backlog Grooming: Is the process to prioritize, define, and estimate User Stories. At this stage coarse grained stories are broken down into smaller discrete User Stories in conjunction with Ways of working document (typically avoiding User Stories being greater than 5 elapsed days of time). The backlog of well-defined User Stories typically using Behaviour Driven Definition (BDD) (Given-When-Then) needs to be ready to “play” ahead of each Sprint cycle. Backlog Grooming is an activity executed in parallel with the Sprint development (even if the first backlog grooming occurs before the first sprint in order to be able to start the development) and it is owned by the Product Owner, helped with input from the Development Team or dedicated Business Analysts. The estimation of User Stories is usually made using Planning poker, by comparing sizes and by opening discussion within the team to agree on what the correct estimate feels (a unit of estimation called a Story Point can be used). It is not mandated to use this but the approach simplifies the estimation process, over time the team becomes better at estimations and in conjunction with their velocity can start to provide an accurate view of delivery.

Prioritization: The sequence of the backlog is determined by a few factors (1) needs priorities of the customer, (2) inter-dependencies on other teams in large projects (3) logic Technical implementation sequence. It is the responsibility of the Product Owner to manage this or Business Analyst with input from the Development team.

Scope changes: At its core Agile embraces change however extra care and management is needed for fixed-price projects to fulfill the commercial agreements.

written by: Eccles,
Gherardini, Magni,
Slager
unit:

approved by: Manuela
Nelli

issue date:

review

page: 15/22



- **Fixed Price Projects:** Increase scope will need to managed through agreed Change Request Processes for fixed-price projects to either increase the remit of the project (extra payment) or trade (1 User Story in and 1 User Story out of equivalent size/complexity).
- **Time & Material Projects:** This does not really matter however you should never change the scope of story that is in Sprint development.

Output Document	Distribution	Template Code
Sprint Planning Meeting minute	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-SPM
Sprint Backlog	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-SB
Product Backlog	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-PB
Sprint Review Meeting minute	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-SRM
Project Closure/State Report	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-PSR
Sprint Retrospective	INTERNAL Usually internal, sometimes can be shared with the customer	REPLY TEMPLATE: REY-AGILE-RETRO
In Delivery User Stories	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-DEL
Production Delivered User Stories (log of released work Done)	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-PDUS
Acceptance Test Report (acceptance of the production release)	EXTERNAL Shared with the customer	REPLY TEMPLATE: REY-AGILE-ATR

written by: Eccles,
Gherardini, Magni,
Slager
unit:

approved by: Manuela
Nelli

issue date:


review

page:

16/22



3.3 Closure

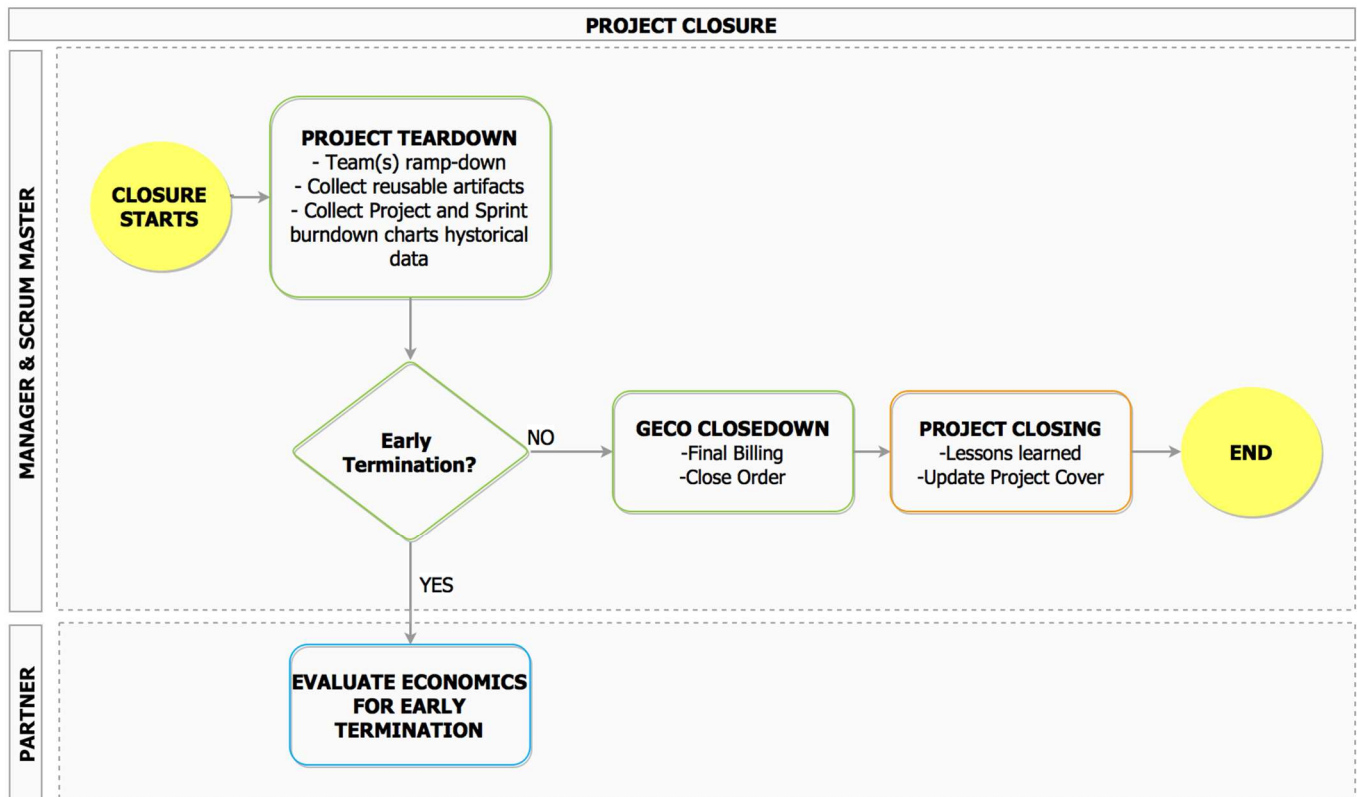

Actors

- **Scrum Master and Development Team:** they are responsible for the technical activities for project teardown
- **Manager (Delivery Manager):** is responsible for the GeCo order closure activities
- **Partner:** is involved in the closure of GeCo orders for large projects and to manage early termination scenarios

Project Teardown: The Scrum Master releases the Development Team as development activities end.

The Development Team collects the non-customer sensitive data onto to be shared with future projects, such as:

- development practices that empowered the Team and allowed them to manage the uncertainty of Agile
- knowledge about successful tools, introduced for the project and not already an asset for the Company
- newly developed libraries, experience on API and frameworks, notable code snippets to apply patterns
- historical delivery evidence such as burndown, velocity, estimation variance

Early Termination: The Manager evaluates if there are the conditions to consider the project as closed in advance, if so the Manager involves the Partner accountable for the project, for further evaluations.

Evaluate economics: The Partner evaluates the Offer against the condition for termination, discussing with the Customer an agreement to handle the case with a common advantage.

written by: Eccles,
Gherardini, Magni,
Slager
unit:

approved by: Manuela
Nelli

issue date:

review

page: 17/22



GeCo Closedown: The Manager (sometimes with the help of the Scrum Master) performs all the activities to close the suborder(s) and the enclosing order.

Project closing: The Manager collects the lessons learned for the sake of future projects. The Manager and the Scrum Master compose and share the updating of the Project Cover.

Output Document	Distribution	Template Code
Project cover	EXTERNAL Shared with the customer	No template provided, Project cover must be compiled on Tamtamy



4 TOOLS & PRACTICES

Nowadays many tools are available for the management of Agile projects from large-scale agile tools through to very simple ticketing boards, with several open source products too. Like with any product to be used for delivery the choice of tool needs to be agreed with the client and the management of the data to be considered sensitive.

One of the tools of choice is Jira from Atlassian, originally a defect management tool that has been converted and considered to be one the most popular tools on the market today for managing Scrum.

This section provides a worked example using Jira to help visualize some of the concepts presented in the document.

4.1 Using Jira Example

4.1.1 Introduction

JIRA platform implements the Scrum framework and it is built for deliver Agile project execution and monitoring. Starting from well-defined processes, schemes and workflows, JIRA allows users to manage and plan activities, issues management and reporting.

As a rule, in accordance to Agile principles, keeping things simple and avoiding replicating waterfall is what is required, an over-complex workflow is going to slow down the team.

As reference a common set of Core Jira terms are provided below:

Jira Concept	Description	Reference
VERSIONS	Versions are points-in-time for a project. They help schedule and organize releases.	Defining Versions
ISSUES	Issue is the base element in JIRA. It could represent a software bug, a project task, a User Story, a helpdesk ticket, a change request and so on.	What is an Issue
WORKFLOWS	A JIRA workflow is the set of statuses and transitions that an issue goes through during its lifecycle.	Defining Workflows
ROLES	A role is a flexible way to associate users and/or groups with a project. Project roles have specific members. Users may play different roles in different projects.	Defining Roles

4.1.2 Mapping processes and document on Jira

Starting from Fixed Price Variable Scope Economic Offer (MDU_SAL_x20) document, below are defined mappings and conventions used on JIRA to address and expose Agile concepts. For each required document, below table specifies how to create it and how is mapped on JIRA:

written by: Eccles, Gherardini, Magni, Slager	approved by: Manuela Nelli	review
unit:	issue date:	page: 19/22



Document	Jira Mapping
Kick-Off (Event)	
Product Backlog (Definition) (REY-AGILE-PB)	JIRA integration is done through customizing User Story building and refinement as defined in Product Backlog
User Stories Definition (Definition) (REY-AGILE-USD)	JIRA integration requires creating and customizing User Story Type with all fields defined in related document
Sprint Planning Meeting (Iterative event)	
Sprint Planning Meeting (REY-AGILE-SPM)	JIRA integration requires creating Sprint by adding User Stories on it, as defined in Sprint Planning Meeting . Sprint Planning on JIRA should be reported on related document
Product Backlog (Refinement) (REY-AGILE-PB)	JIRA integration is done through customizing User Story building and refinement as defined in Product Backlog
Sprint Review Meeting (Iterative event)	
Sprint Review (Acceptance) Meeting (REY-AGILE-SRM)	JIRA integration requires defining and exporting Sprint Reports as defined in Sprint Review . Charts export should be reported on related document
Product Backlog (Refinement) (REY-AGILE-PB)	JIRA integration is done through customizing User Story building and refinement as defined in Product Backlog
Production Delivery	
In-Delivery/Deliverable User Stories (REY-AGILE-DEL)	JIRA integration is done through moving User Story to the "Delivery" and "Delivered" state
Production Delivered User Stories (Refinement) (REY-AGILE-PDUS)	JIRA integration requires exporting User Stories in "Delivery" and "Delivered" state

4.1.3 Backlog Hierarchy (Epics -> User Stories -> Tasks)

Within Jira the hierarchy of EPICs to User Story to Tasks exists for the main backlog development. Typically

- EPICs should be used as placeholders and themes by which to get an overall view of progress.
- User Stories to be discrete deliverables to be witnessed by the customer
- Tasks are for the teams to manage the work through the breakdown of explicit work items to fulfill the user stories.

NOTE: In Jira EPICs are like specialized Labels but allow for visualization of completion of their child User Stories.

The overall workflow for the User Stories can be customized by highly recommended to keep simple, here is an example workflow from User Story creation through to delivery into Live.

written by: Eccles,
Gherardini, Magni,
Slager
unit:

approved by: Manuela
Nelli

issue date:


review

page: 20/22



4.1.4 Sprint Planning

Planning activity is by default provided on JIRA by simply moving Stories from actual Backlog to one of the available Sprints. Usually, target Sprint is the next one to be started. Stories can be moved only into waiting Sprints.

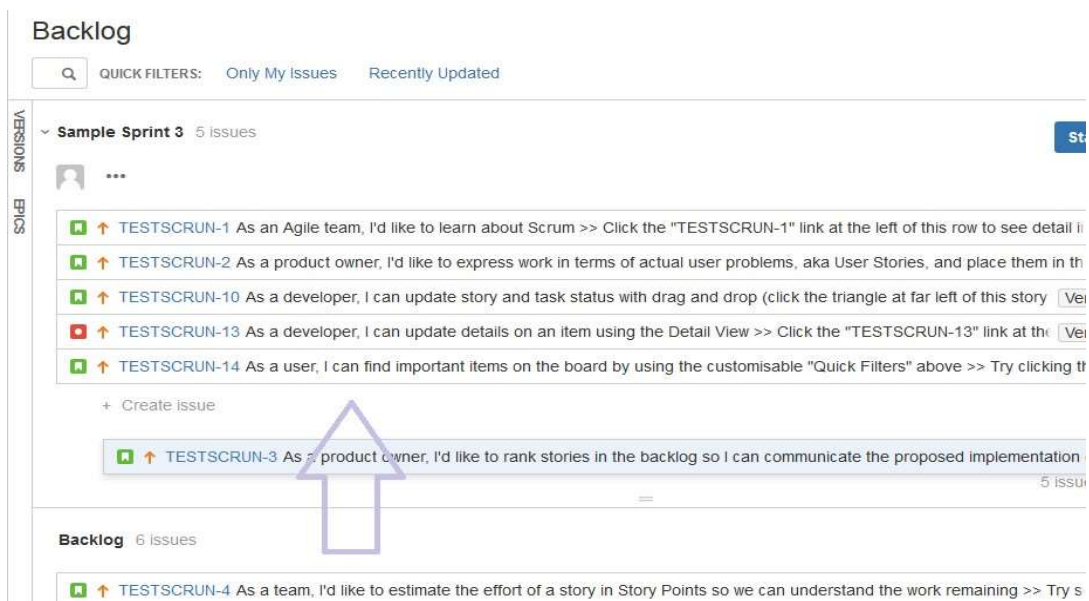

Once Sprint creation and planning has finished all activities, Stories chosen and effective next Sprint plan are required to be reported on REY-AGILE_SPM.docx document.

4.1.5 Sprint Review

Review process uses JIRA exports and reports to provide information, trends and activities occurred during Sprint execution.

written by: Eccles,
Gherardini, Magni,
Slager
unit:

approved by: Manuela
Nelli
issue date:

review

page: 21/22



All required exportable items and charts are reported in REY-AGILE_SRM.docx document. This document should hence be filled with JIRA charts export as well as Stories list and status.

4.2 GeCo Management

At the start of the project, it is necessary to create the GeCo order and suborders according to some specific guidelines.

Create a new job order or use an existing job order in order to aggregate all correlated activities/projects by avoiding to create a new job order for each job sub order.

GeCo Order Setup. For pure Agile project, without any significant up front discovery phases, **if the project lasts more than 3 months, we have to split the projects in 2 different job suborders:**

- the first one for covering the sprints included in the first 3 months
- the second one for covering the sprints foreseen for the following months.

This high level splitting is necessary to avoid to plan in GeCo (and in CoGe) a budget too variable for the next months according to the level of variance of the backlog. Since, usually in the agile, the backlog is more stable and detailed for the near sprints, it is more reliable to split stable revenue and people planning for near activities, and postpone the uncertainty to the more far sprints.

The first suborder must contain the budget and people planning related to the backlog/sprints in working in the next 3 months sprints; the second suborder must contain residual budget and the planning of the rest of the project.

The “Agile flag” **must be set** in the overall order and child suborders.

In case of Large Scale Agile Project, it is also advisable to split out suborders to represent the Project Structure, to keep the costs manageable, for Example the “Demand” team could be a suborder.

GeCo Order Updating. At the end of each sprint, planning and potentially also the budget must be updated according to the backlog evolution. In case of multiple agile suborders, at the end of each month, both the suborders (near and far) must be updated. If the backlog is becoming clearer and detailed about the 4th month, the related budget and people planning, must be transferred in the first suborder.

GeCo Order Closing. The project closure activity follows the standard management of GeCo, in general the closure is the same however in the case of Agile methodology it is more likely that changes come in to extend the project as such a view would need to be taken on whether the existing suborders are extended or new ones created.

written by: Eccles,
Gherardini, Magni,
Slager
unit:

approved by: Manuela
Nelli

issue date:

review

page: 22/22
